

Job No: P26034  
 Name: MATTHEWS

Address:

Tel:


Sheet: 1 of 1

Faux Silk

Col FAU 026

Loft Bed  
 =  $380 \times 500$   
 =  $19m^2$

RAISED BASE - PAINTED - No CPT Here.

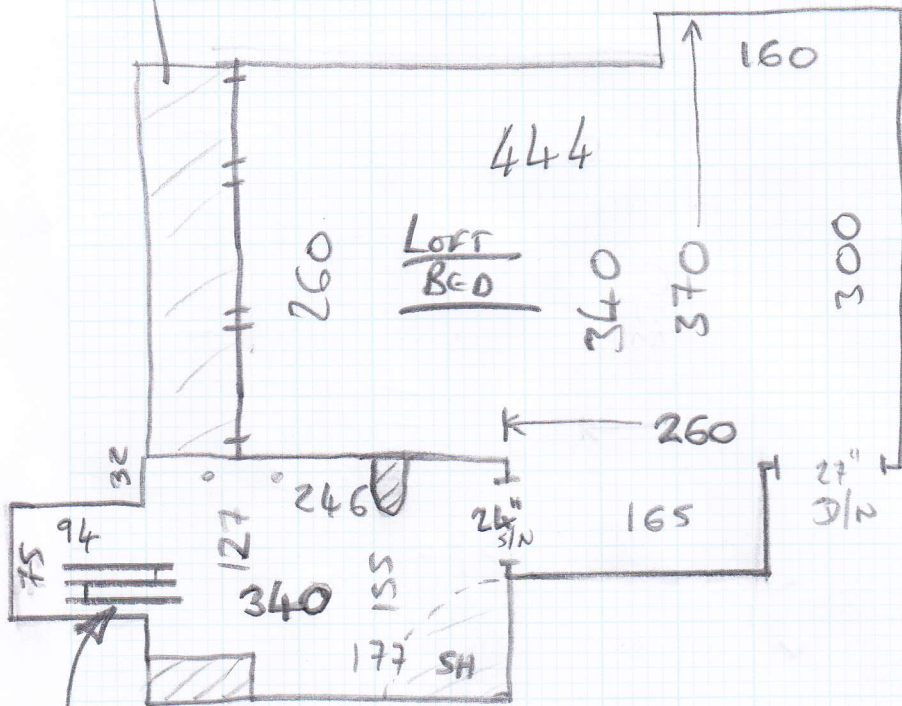

\* Lay H/BOARD and  
 \* Fit C/Flor with Planks  
 Running lengthways.  
 Apply mastic Seal to  
 perimeter & around fittings.

Rhinoflex options

Timber - FARMHOUSE WHITE  
 2081

Loft BATH -  $350 \times 200$   
 =  $7m^2$
