TRANSFORM
ETHNIC
WENGE
28160

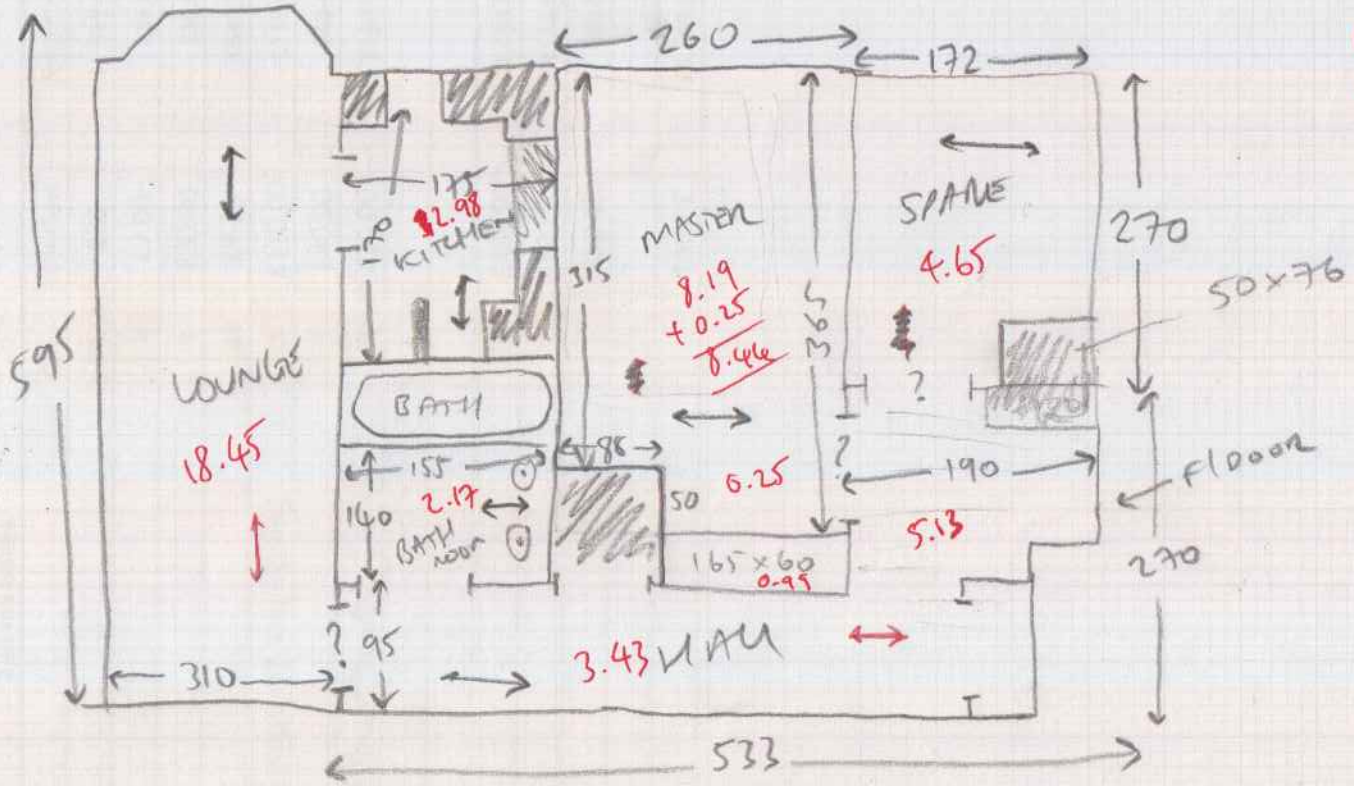

OVERLAY
46.24 NETT METRES
3.62 SQM BOXES
13 BOXES = 47.06
BETTER TO ORDER
14 BOXES = 50.68

FLAT TO BE RENOVATED COMPLETELY

APPEARS TO BE APPROX 18mm CHIPBOARD SUBFLOOR

FULL PLYWOOD PREP THROUGHOUT

RUN INTO DOORWAYS SEAMLESSLY - DISAR WILL BE NEEDED @ LOUNGE ONLY
- CUSTOMER ORGANIZING?

LAMINATE DOWN EVERYWHERE.

~~BATHROOM HAS TILES. SELF LEVELLER OVER LEFT OVER TILE ADHESIVE~~
~~TO RIP UP IN KITCHEN~~
