Name	Duration	Start	Finish
Aylesham	**30w**	**03/04/2023**	**06/11/2023**
Superstructure	**11w 4d**	**03/04/2023**	**28/06/2023**
Installation of Stone	3w	03/04/2023 *	25/04/2023
Completion of brick & blockwork	3w	03/04/2023	25/04/2023
Roof Coverings	5w	03/04/2023	10/05/2023
Fit Hopper heads & related	2w	26/04/2023	10/05/2023
Install Mansafe & PV	2w	26/04/2023	10/05/2023
Strike Scaffold to 1st Floor	1w	11/05/2023	17/05/2023
Fit Guttering Downpipes	3d	18/05/2023	22/05/2023
Window lead time	8w	03/04/2023 *	01/06/2023
Fit First Floor Windows inc Mastic	4d	02/06/2023	07/06/2023
Clean Down Brickwork 1st and 2nd Floor	1w	08/06/2023	14/06/2023
Strike Remaining Scaffold	3d	15/06/2023	19/06/2023
Install Ground Floor Winsows and Doors	1w	20/06/2023	26/06/2023
Clean Down Brickwork to Ground Floor	2d	27/06/2023	28/06/2023
Finishings	**29w 2d**	**03/04/2023**	**31/10/2023**
Electrical First Fix	4w	03/04/2023 *	03/05/2023
Carpentry 1st Fix	2w	03/04/2023	18/04/2023
UFH to Garage / Pool Wing	3w	02/05/2023	22/05/2023
Screed to Garage / Pool Wing	3w	02/05/2023	22/05/2023
First Floor	**22w**	**03/04/2023**	**08/09/2023**
Install flues, Insulation to loft space etc	3w	03/04/2023 *	25/04/2023
Fit Delta Track lighting & board ceilings to FF	3w	24/04/2023	15/05/2023
Skim to FF, including skirt & shadow gap detailing	3w	09/05/2023	30/05/2023
Mist Coat to FF	1w	25/05/2023	01/06/2023
Wall & Floor tiling FF	3w	02/06/2023	22/06/2023
Wood Floor FF (Master Suite)	2w	07/06/2023	20/06/2023
Carpentry mid fix FF	2w	12/06/2023	23/06/2023
Plumbing mid fix FF	2w	16/06/2023	29/06/2023
Electrical mid fix FF	2w	21/06/2023	04/07/2023
Decoration FF	4w	23/06/2023	20/07/2023
Fitted Furniture FF	2w	21/07/2023	03/08/2023
Carpentry finals FF	2w	04/08/2023	17/08/2023
Plumbing finals FF	2w	11/08/2023	24/08/2023
Electrical finals FF	2w	11/08/2023	24/08/2023
Decoration finals FF	2w	18/08/2023	01/09/2023
Carpets FF	1w	04/09/2023	08/09/2023
Ground Floor	**19w 2d**	**16/05/2023**	**29/09/2023**
Fit Delta Track Lighting & board ceilings to GF	3w	16/05/2023 *	06/06/2023
Skim to GF	3w	31/05/2023	20/06/2023
Mist Coat to GF	1w	21/06/2023	27/06/2023
Floor & Wall tiling GF	4w	28/06/2023	25/07/2023
Wood Floor GF	3w	07/07/2023	27/07/2023
Carpentry mid fix GF	2w	20/07/2023	02/08/2023
Plumbing mid fix GF	2w	20/07/2023	02/08/2023
Electrical mid fix GF	2w	27/07/2023	09/08/2023
Decoration GF	4w	28/07/2023	24/08/2023
Kitchen GF	1w	25/08/2023	01/09/2023
Fitted Furniture GF	2w	04/09/2023	15/09/2023
Carpentry finals GF	2w	11/09/2023	22/09/2023
Plumbing finals GF	2w	11/09/2023	22/09/2023
Electrical finals GF	2w	11/09/2023	22/09/2023
Decoration finals GF	2w	18/09/2023	29/09/2023
Carpets GF (Cinema)	2d	28/09/2023	29/09/2023
Garage & Pool Wing	**23w 4d**	**16/05/2023**	**31/10/2023**
MF Ceilings to Garage & Pool	3w	16/05/2023	06/06/2023
Tack & Skim to Garage & Pool	4w	07/06/2023	04/07/2023
Mist Coat Garage/Pool	2w	28/06/2023	11/07/2023
Floor & Wall tiling Garage & Pool	6w	05/07/2023	15/08/2023
Wood to stairs - Garage	3w	02/08/2023	22/08/2023
Carpentry mid fix Garage & pool	3w	02/08/2023	22/08/2023
Plumbing mid fix Garage & Pool	3w	09/08/2023	30/08/2023
Electrical mid fix Garage & Pool	3w	09/08/2023	30/08/2023
Decoration Garage & Pool	4w	16/08/2023	13/09/2023
Kitchen Garage Annex	1w	14/09/2023	20/09/2023
Fitted Furniture Garage & Pool	1w	21/09/2023	27/09/2023
Carpentry finals Garage & Pool	2w	27/09/2023	10/10/2023
Plumbing finals Garage & Pool	2w	04/10/2023	17/10/2023
Electrical finals Garage & Pool	2w	04/10/2023	17/10/2023
Decoration finals Garage & Pool	2w	11/10/2023	24/10/2023
Carpets - Annex & Gym Floor	1w	25/10/2023	31/10/2023
Swimming Pool Fit Out	10w	23/05/2023	01/08/2023
Sauna & Steam	4w	03/07/2023	28/07/2023
Externals	**18w**	**29/06/2023**	**02/11/2023**
Drainage	4w	29/06/2023	26/07/2023
Hard Lanscaping	16w	13/07/2023	02/11/2023
Soft Landscaping	8w	01/09/2023	26/10/2023
Fencing	2w	01/09/2023	14/09/2023
Handover	**7w**	**18/09/2023**	**06/11/2023**
Commission	4w	18/09/2023	13/10/2023
Mastic	1w	18/09/2023	22/09/2023
Snag	7w	18/09/2023	03/11/2023
Building Control Certification	2d	02/11/2023	03/11/2023
Handover		06/11/2023	06/11/2023

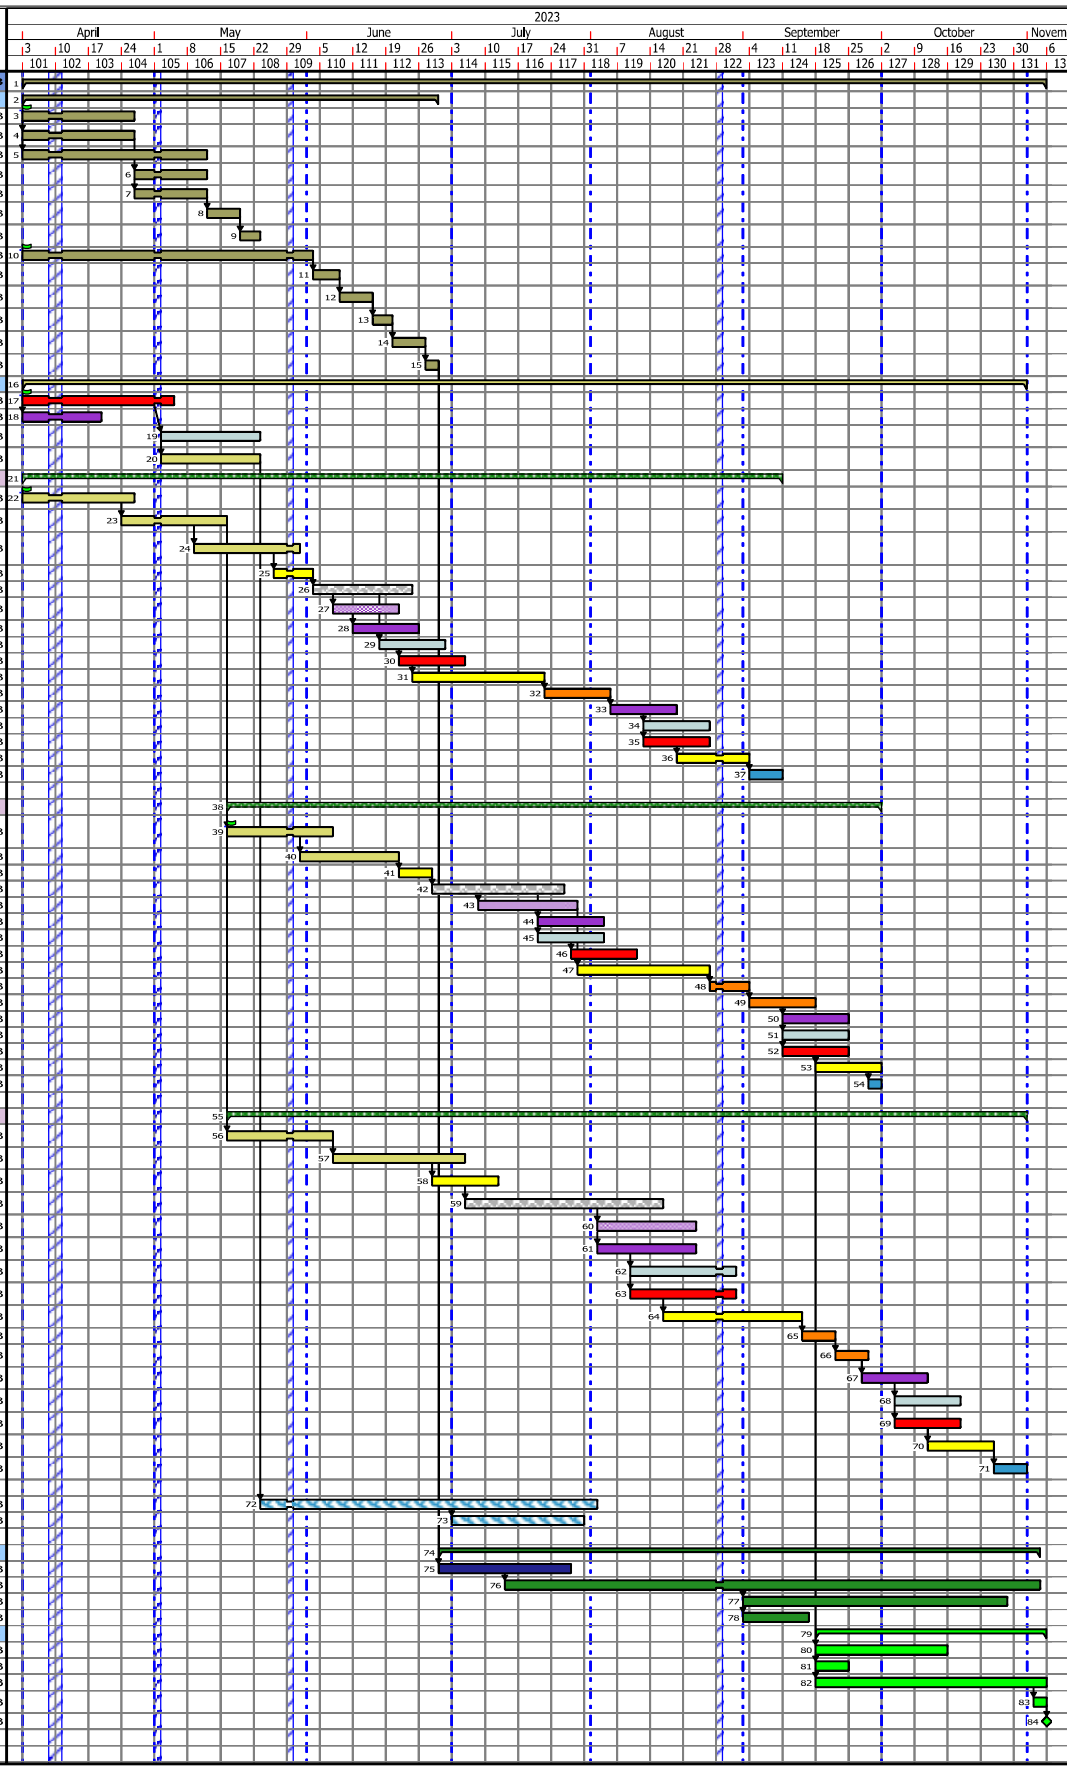

les Contractor

Superstructure | Plasterworks & screed | Electrical & AV | Carpentry | Plumbing/ Heating | Decoration | Tiling
Wood Flooring | Fitted Furniture | Carpets | Swimming Pool | Externals | Groundworks | Commission & Snag
